

Project Planning Phase-IV

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

Date04 October 2026

Team ID

Project NameImplement Client Script & UI Policy (Incident)

Product Backlog, Sprint Schedule, and Estimation

The backlog below plans the previously defined Incident-form requirements across three short implementation sprints.

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Incident Form Validation	USN-1	Validate required incident information before submission.	3	High	Member 1
Sprint-1	Incident Form Validation	USN-2	Display alerts or field messages for incomplete or invalid input.	2	High	Member 2
Sprint-1	Dynamic Field Behaviour	USN-3	Make fields mandatory based on incident conditions.	2	High	Member 3
Sprint-2	Dynamic Field Behaviour	USN-4	Show or hide fields based on category, priority or state.	3	High	Member 1
Sprint-2	Dynamic Field Behaviour	USN-5	Make selected fields read-only when defined conditions are met.	2	High	Member 2
Sprint-2	Client-side Field Handling	USN-6	Clear irrelevant values when a controlling field changes.	2	Medium	Member 3
Sprint-3	Client-side Field Handling	USN-7	Auto-populate related values where appropriate.	3	Medium	Member 1
Sprint-3	User Guidance	USN-8	Provide contextual field-level guidance for important inputs.	2	Medium	Member 2
Sprint-3	Testing & Validation	USN-9	Test Client Scripts and UI Policies for expected and conflicting conditions.	3	High	All Members

Project Planning Phase-IV

Project Tracker & Velocity

Project Tracker

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed	Sprint Release Date (Actual)
Sprint-1	7	5 Days	05 Oct 2026	09 Oct 2026	7	09 Oct 2026
Sprint-2	7	5 Days	10 Oct 2026	14 Oct 2026	7	14 Oct 2026
Sprint-3	8	5 Days	15 Oct 2026	19 Oct 2026	8	19 Oct 2026

Velocity

Total backlog: 22 story points across 3 sprints and 15 working days.

Average sprint velocity: $22 \div 3 = 7.33$ story points per sprint.

Average daily velocity: $22 \div 15 = 1.47$ story points per working day.

Sprint Summary

Sprint	Planned Focus	Story Points	Expected Outcome
Sprint-1	Validation + mandatory rules	7	Core data-entry validation operational
Sprint-2	Visibility/read-only + value clearing	7	Dynamic field behaviour operational
Sprint-3	Auto-population + guidance + testing	8	Integrated solution tested and ready

Project Planning Phase-IV Burndown Chart

Burndown Chart

The burndown chart represents work remaining over the planned 15-day implementation period for the 22-point backlog.

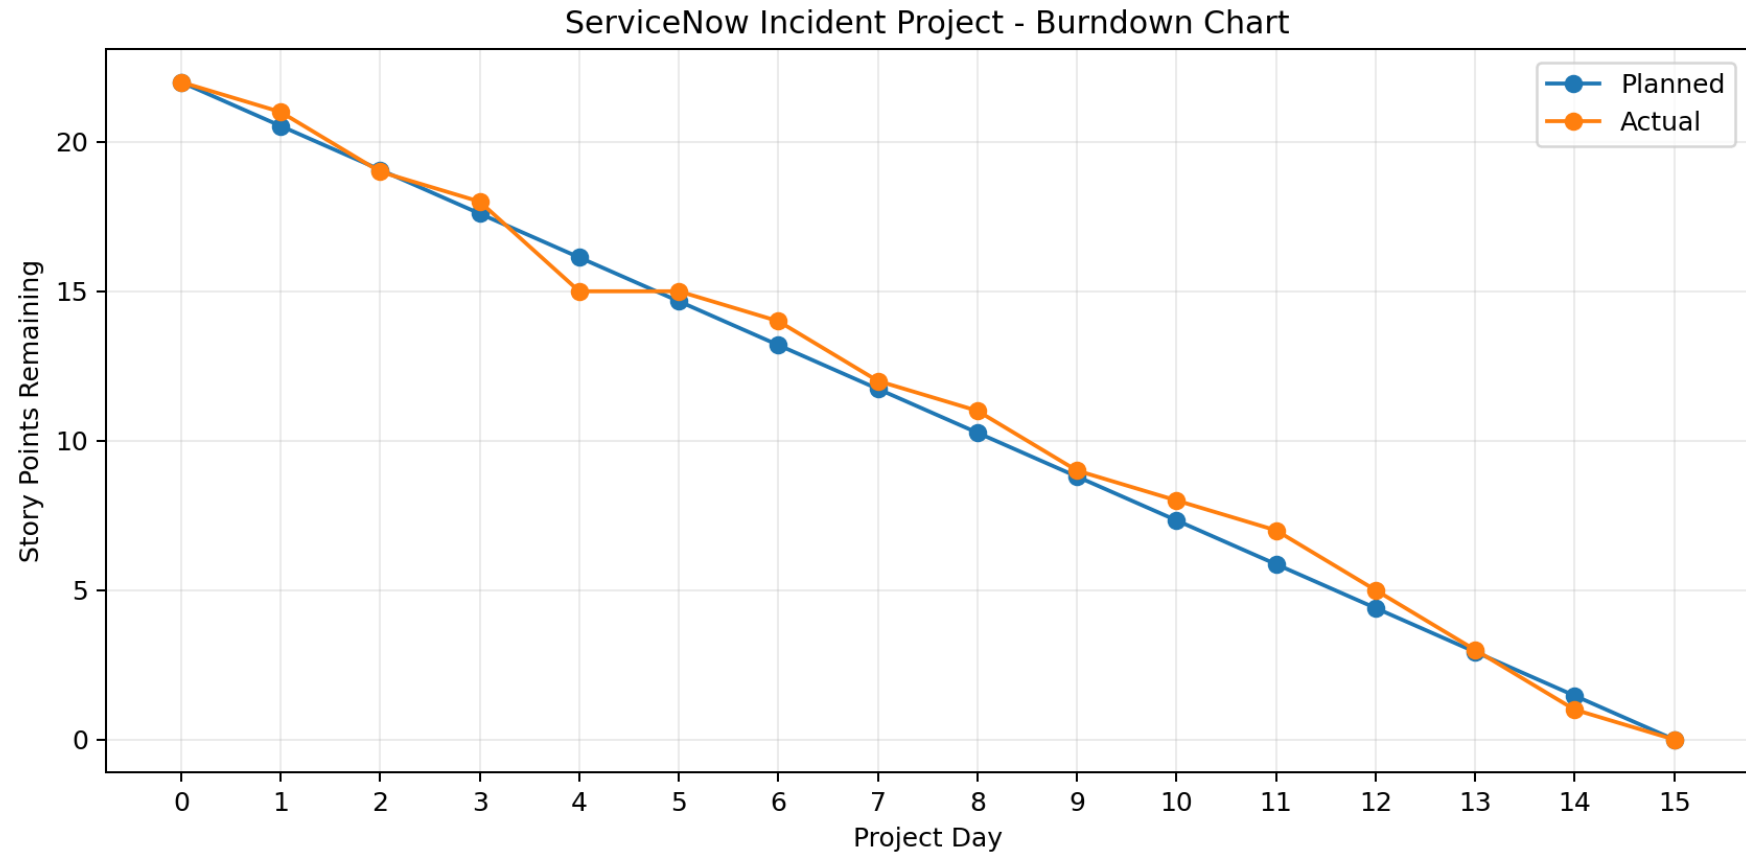


Figure 1: Planned versus illustrative actual story points remaining

Interpretation: The planned line reduces steadily from 22 to 0 points. The illustrative actual line shows small variations during implementation while still reaching zero by the planned project end.
